Boscastle, Bossiney & Tintagel STS
Construction Programme

ID	Task Name
1	**Contract**
94	**Site Mobilisation**
95	F10 Updated with BNL details
96	Project Management Plan and Method statements
97	Install Setting control stations along Pipe routes
98	Trial Holes to locate Water main all hand dig
99	Setup site compounds STW/Forrabury/Pipeline
100	**Construction Phases**
101	**Pipelines**
102	Trevalga STW to Trethevy
103	STW Road Crossing
104	Forrabury to Trevalga STW (Trevalga Fete 17/7/09 No work till 19th either side of Hamlet)
105	Welltown Road section
106	Road section Trethevy to Bossiney September 09
107	Bossiney to Back lane PS (Note Tintagel Battle Event first weekend in August)
108	Bossiney Outfall Access
109	Bossiney Outfall Extension Note need to use Spring Tides around 20th Aug & 20th Sept
110	Back lane PS to outfall
111	Back Lane PS to Tintagel (Compound Bill Dangar's field)
112	Tintagel to Castle rd PS
113	Castle Rd PS to Tintagel Haven (Evening work)
114	Forrabury to New Road PS (Compound At Forrabury
115	New Road PS to Boscastle Quay PS
116	**Pump Stations**
117	Forrabury PS
118	Back Lane PS
119	Castle Rd PS
120	Haven PS
121	New Road PS
122	Boscastle Quay PS
123	**STW**
124	Bulk Excavation including re-profile of Field
125	Excavation & Shoring for Galglass Tank
126	Galglass Aeration Tank
127	Inletworks & Control Building
128	Re-circulated & Surplus Activated Sludge (RAS/SAS) Pump Chamber
129	35m3 SelectorTank Chamber
130	Works Re-circulated Liquors Pump Chamber
131	Sludge Plant
132	Site Ducting & Cables
133	MCC Install
134	Aeration Plant Mechanical Install
135	Installation of Mixers & Pumps
136	Blowers installed
137	Odour Control slab and NES install
138	Final Finishes / Roads / Drainage / Steelwork
139	Commissioning & seeding of Aeration tank
140	Landscaping (Note Landscaping to top field prior to end of September 09 if possible)

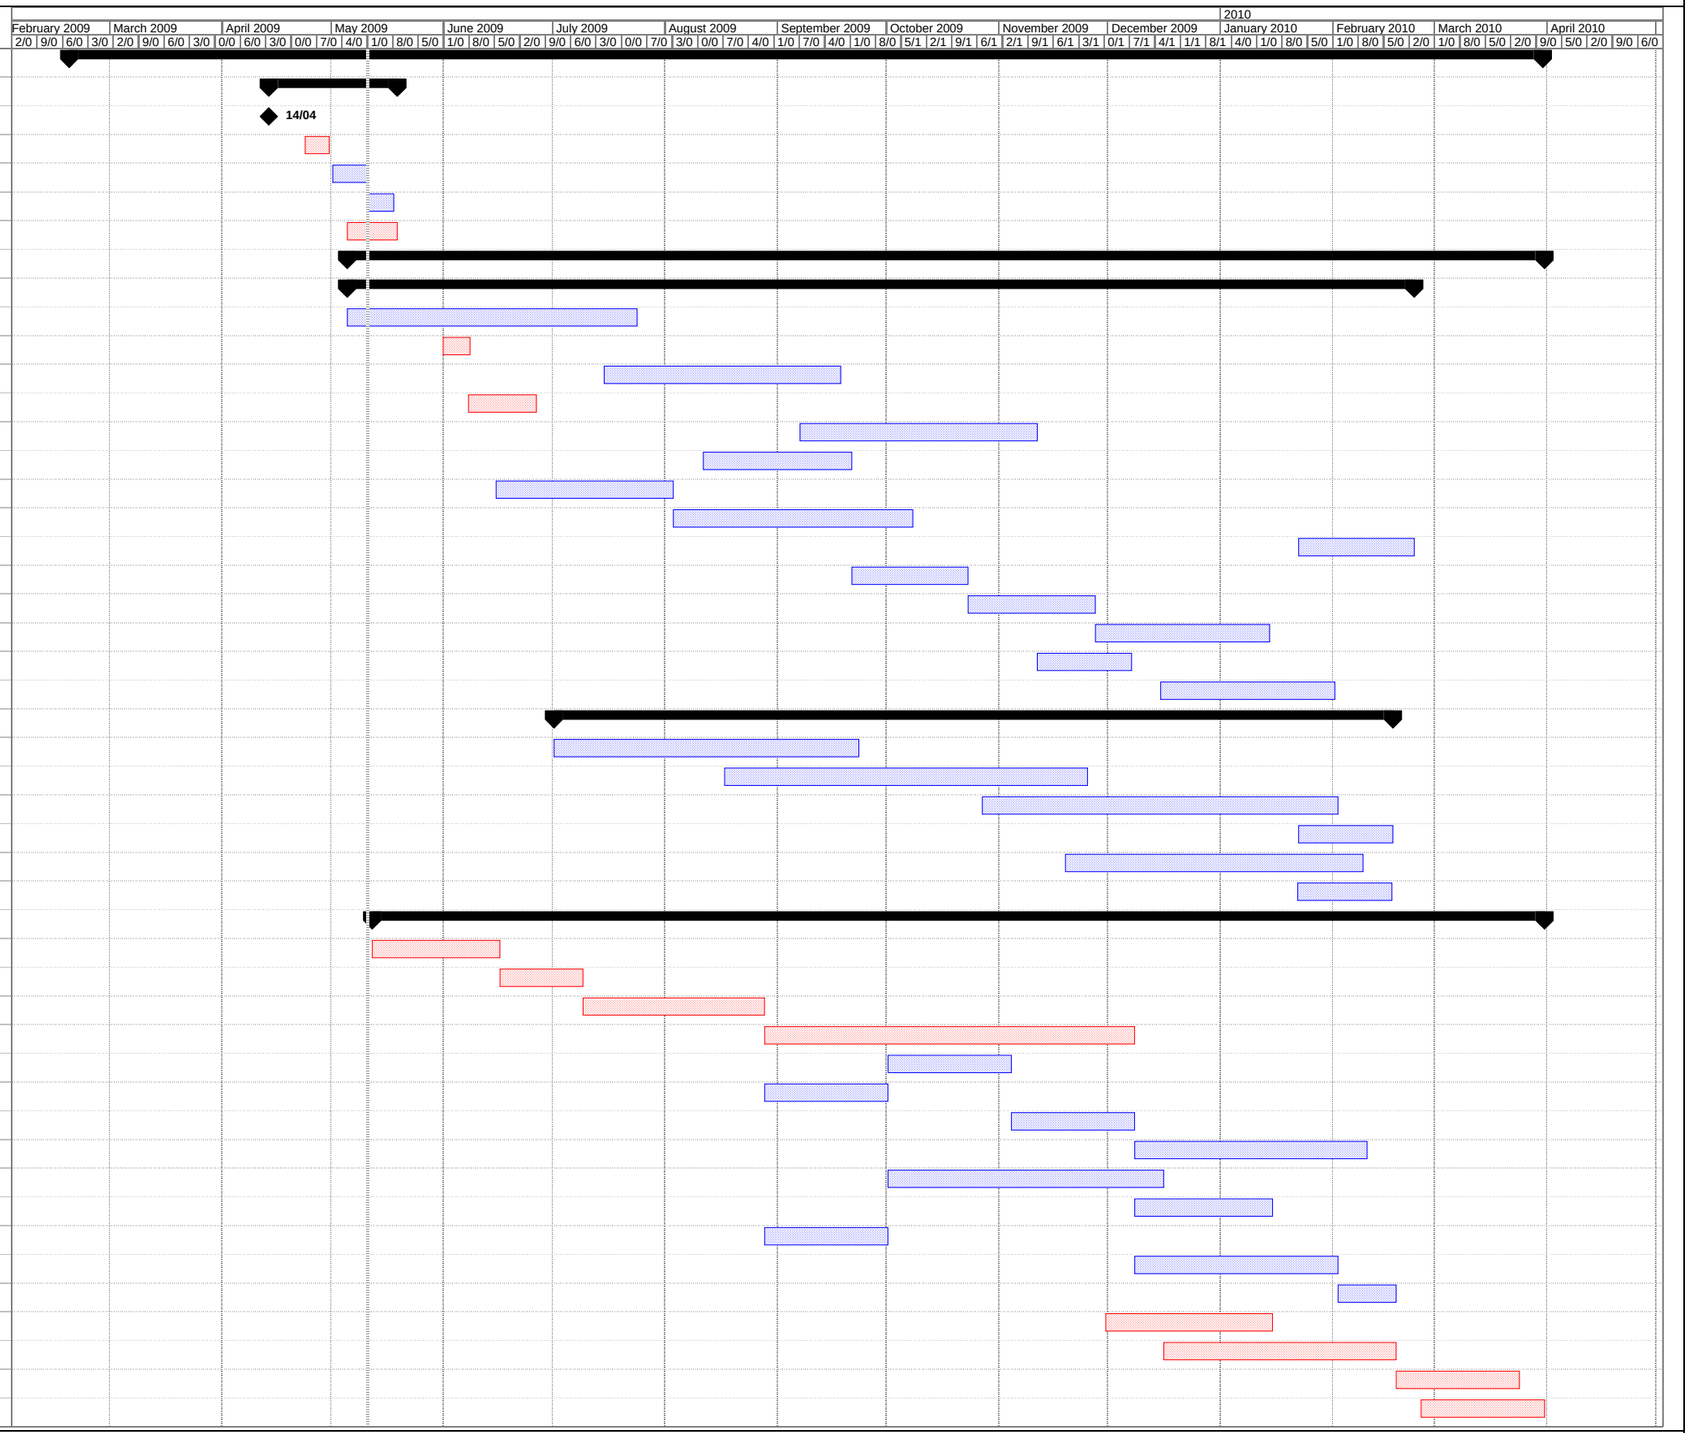

Project: RMB BBT Flood Defence Sch
Date: Mon 11/05/09

Task | Critical Task | Progress | Milestone | Summary | Rolled Up Task | Rolled Up Critical Task | Rolled Up Milestone | Rolled Up Progress | Split | External Tasks | Project Summary | Group By SummTask | Critical Task

BAM Nuttall Limited
Pre-Construction Programme Rev E 27-04-09
